
Prayog — Timeline and Gantt Chart

CS455 Deliverable 3 · Group 3 · 6 November 2026

1. Gantt chart

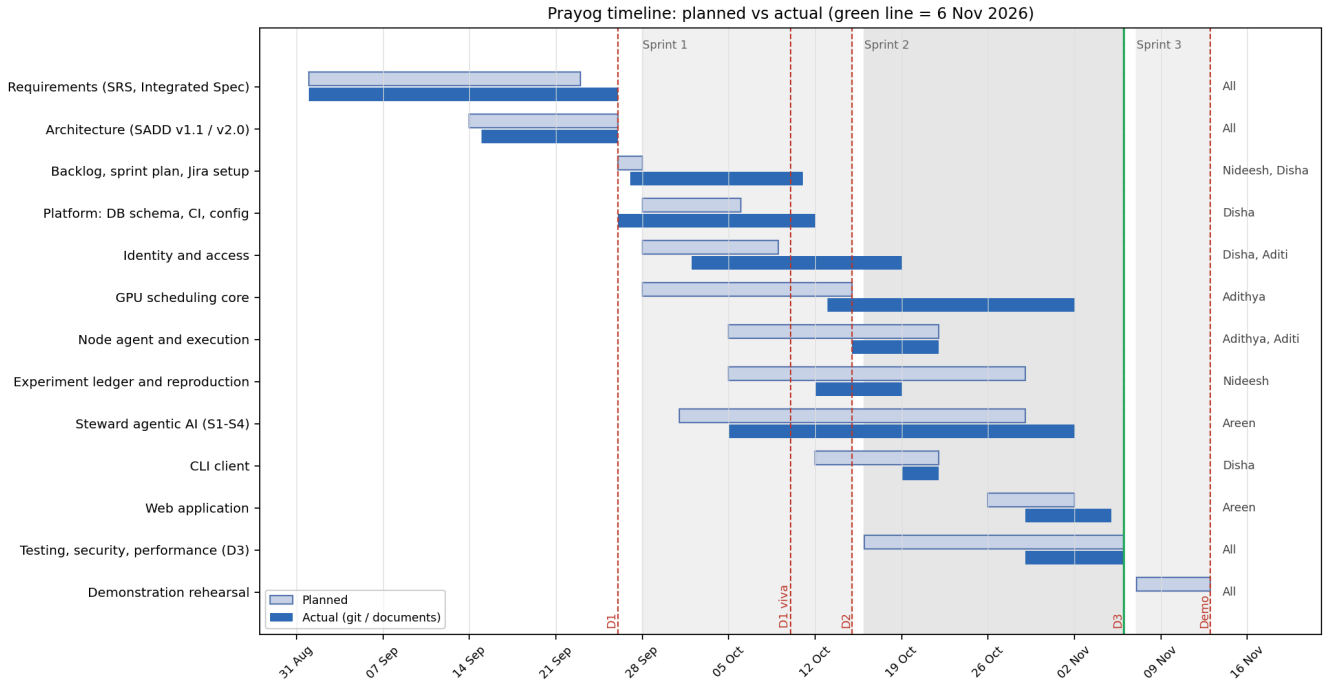

Planned bars come from the sprint plan (`PRAYOG_Backlog_and_Sprint_Plan.md`, 27 Sep). Actual bars come from the repository: first and last commit on `main` touching each subsystem's code (`git log -- <path>`), and from document dates for the pre-sprint phases (requirements and architecture start dates are approximate; their end dates are the D1 documents' dates).

2. Milestones

Milestone	Planned	Actual	Notes
D1 — requirements and architecture	26 Sep	26 Sep (submitted with SADD v1.1)	SADD v2.0 written 26 Sep, not in the submission
D1 viva	10 Oct	10 Oct	
Sprint 1 planning	28 Sep	28 Sep	Jira populated by bulk import on 11 Oct
D2 — implementation, Agentic AI, sprint execution	15 Oct	15 Oct	Steward merged (PR #11); ledger integrated (10 working-repository PRs)
Sprint 2 planning	16 Oct	16 Oct	
CLI complete	22 Oct (plan: Sprint 2)	22 Oct (PR #25)	
Web application for all roles	not in the plan	5 Nov (PR #26)	added during Sprint 2
D3 — testing, security, performance, cost, deployment, reliability	6 Nov	6 Nov	this package
Demonstration	8–13 Nov	—	Sprint 3

3. Planned vs actual, by workstream

Workstream	Planned	Actual (git)	Slip	Why
Platform: schema, CI, config	28 Sep – 6 Oct	26 Sep – 12 Oct	+6 days	CI grew with each subsystem (Docker worker, node-agent container)
Identity and access	28 Sep – 9 Oct	2 Oct – 19 Oct	+10 days	access-request `purpose` (PR #19) and CLI login added in Sprint 2
GPU scheduling core	28 Sep – 15 Oct	13 Oct – 2 Nov	+18 days	started late (13 Oct, after the plan's calibration), then claim re-check, bucketed pass and review fixes in Sprint 2
Node agent and execution	5 – 22 Oct	15 – 22 Oct	on time (compressed)	
Experiment ledger and reproduction	5 – 29 Oct	12 – 19 Oct	10 days early	built in a separate working repository and merged as a block
Steward S1–S4	1 – 29 Oct	5 Oct – 2 Nov	+4 days	integration with the real backend, CLI-rebuild gap (D3-01)
CLI client	12 – 22 Oct	19 – 22 Oct	on time	
Web application	26 Oct – 2 Nov (added)	29 Oct – 5 Nov	+3 days	full review and CI repair before merge
Testing, security, performance (D3)	16 Oct – 6 Nov	29 Oct – 6 Nov	started 13 days late	functional work overran; non-functional testing compressed into the last week (retrospective, Project report section 6)

4. Critical path

Requirements → Integrated Specification → GPU scheduling core (claim, pass) → node agent and dispatch → ledger seal hook → Steward diagnosis → web app → D3 testing. The scheduling core was the longest single chain (it gates execution, the ledger's rebuilds and the Steward's inputs); its 18-day slip is what pushed non-functional testing into the final week.

5. Remaining schedule (Sprint 3, 7–13 Nov)

Item	Owner	By
Import D3 bugs into Jira; screenshot the dashboard	team lead	7 Nov
Merge `d3-testing`, then `d3-final` (fixes, scheduler test suite, experiments) through reviewed PRs	Areen, Adithya	8 Nov
Deploy with `docker-compose.deploy.yml` on a cloud VM and run the smoke checklist	team	8 Nov
Demo environment per Deployment guide; rehearsal	all	11 Nov
Demonstration	all	8–13 Nov window
